

### PROJECT ARCHITECT:

MSA Professional Services, Inc.  
Carter Arndt, AIA  
carndt@msa-ps.com

### MSA PROJECT TEAM:

Raine Gardner, PE, Civil Engineer  
Sarah McDonald, PLA Landscape Architect

### AQUATICS SUBCONSULTANT:

Water Technology Inc.  
Matt Freeby

### DATE:

May 3, 2016

### STATUS SUMMARY:

The project development is proceeding on schedule. The Parks and Recreation Committee recently met to review and approve for the project to proceed with final design and bidding. MSA as the Architect/Engineer in collaboration with Water Technology as the Aquatics Designer are proceeding with work on the final drawings and specifications. See the attached rendered overall park plan and aquatics plan.

### COMPLETED PROJECT ACTIVITIES:

<b>February 4<sup>th</sup></b>	Kick-off Meeting #1 conducted
<b>February 10<sup>th</sup></b>	Aquatics Programming, Group Meetings and Tours took place
<b>February 12<sup>th</sup></b>	Draft program statement reviewed and Concept development began
<b>February 18<sup>th</sup></b>	TEAM Conference Meeting
<b>February 24<sup>th</sup></b>	Conceptual Design Meeting #2
<b>February 29<sup>th</sup></b>	Public Open House conducted
<b>March 1<sup>st</sup></b>	TEAM Conference Meeting
<b>March 9<sup>th</sup></b>	Schematic Design Meeting #3
<b>March 16<sup>th</sup></b>	TEAM Conference Meeting
<b>March 21<sup>st</sup></b>	Parks and Recreation Committee Meeting
<b>March 30<sup>st</sup></b>	Stormwater Meeting
<b>April 6<sup>th</sup></b>	Design Development Meeting
<b>April 25<sup>th</sup></b>	DD Civil & additional Parks and Recreation Committee Meeting
<b>April 27<sup>th</sup></b>	DD Meeting - #6
<b>April 29<sup>th</sup></b>	Complete Design Development Package
<b>May 2<sup>nd</sup></b>	Start Final Construction Documents

### UPCOMING PROJECT ACTIVITIES:


<b>May 18<sup>th</sup></b>	Construction Documents Meeting #7
<b>May 20<sup>th</sup></b>	Site Plan Submittal to Community Development
<b>April 27<sup>th</sup></b>	Construction Documents Meeting #8

### PROPOSED OVERALL SCHEDULE:

<b>Construction Document Completion</b>	June 27 <sup>th</sup>
<b>Bidding</b>	July 1-21
<b>Finance Committee Meeting</b>	July 26 <sup>th</sup>
<b>City Council Award</b>	August 3 <sup>rd</sup>
<b>Start Construction</b>	Mid-August
<b>Finish Construction</b>	Late June 2017

Erb Park and Pool Update

City of Appleton, WI  
May 3, 2016

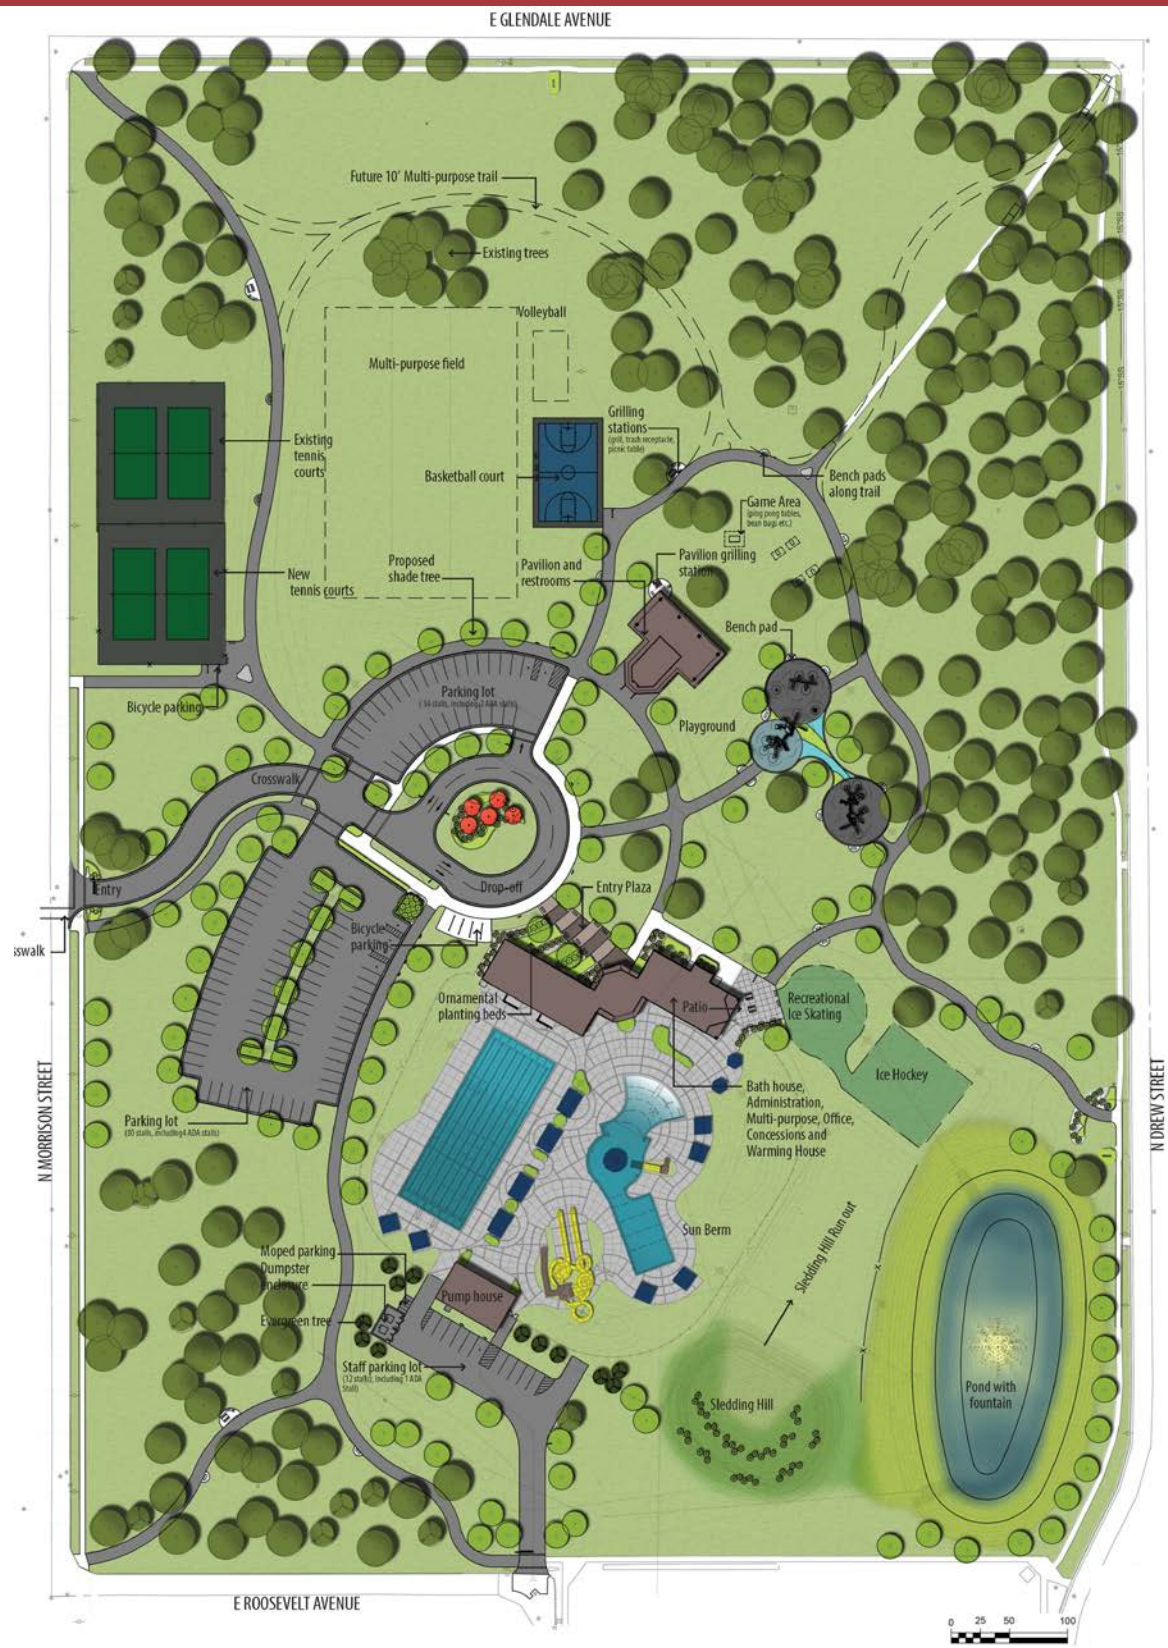



# Erb Park and Pool Update

- 1 ZERO DEPTH ENTRY
- 2 BODY SLIDE TERMINATING IN RUNOUTS
- 3 TOT SLIDE
- 4 25' SLIDE TOWER
- 5 WATER BASKETBALL
- 6 SHADE
- 7 CONCESSIONS PATIO
- 8 SUN TURF
- 9 1M SPRINGBOARD

