



© Skidmore, Owings & Merrill

BOLDT[®]
BUILD BOLDLY

September 2023

SEPTEMBER REPORT

City of Appleton – Appleton Public Library


KEY PROGRESS POINTS

- Office Trailer/Subcontractor's Trailer:
 - Still waiting for power to be hooked-up by WE Energies.
 - Camera will be installed once we have power.
- Recycling Program:
 - Boldt continues to recycle items, as necessary.
 - Weights to date of all metals are 138,000 lbs.
- Progress:
 - Lower-Level demolition was completed and now mechanical, electrical, and plumbing demolition is taking place.
 - Ground Level wall demolition was completed and mechanical, electrical, plumbing, and fire protection demolition has been completed as well.
 - Upper-Level mechanical, electrical, plumbing, and fire protection demolition was completed and CMU wall demolition has begun.
 - Building permit was obtained.

CONDITIONS & SAFETY

- Site conditions are good. Continuously monitoring our safety program and making sure workers and the general public are safe.
- There were no injuries this month.

PROGRESS PHOTOS

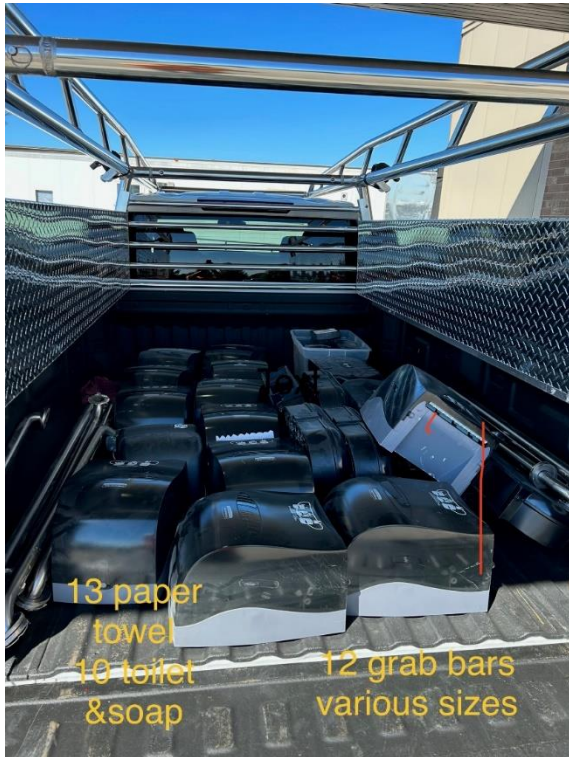

Items salvaged and taken to Restore



Exterior



Exterior




Ground Level


PROGRESS PHOTOS




Northeast Ground Level

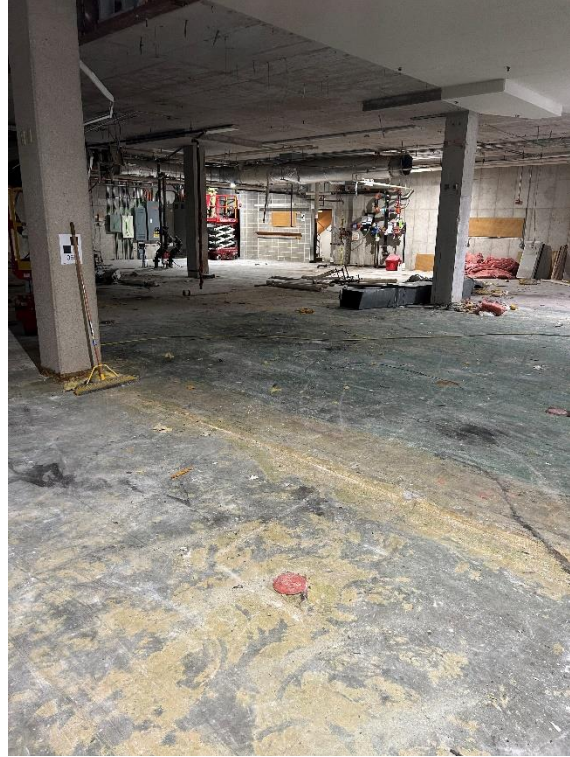

Northwest Lower Level

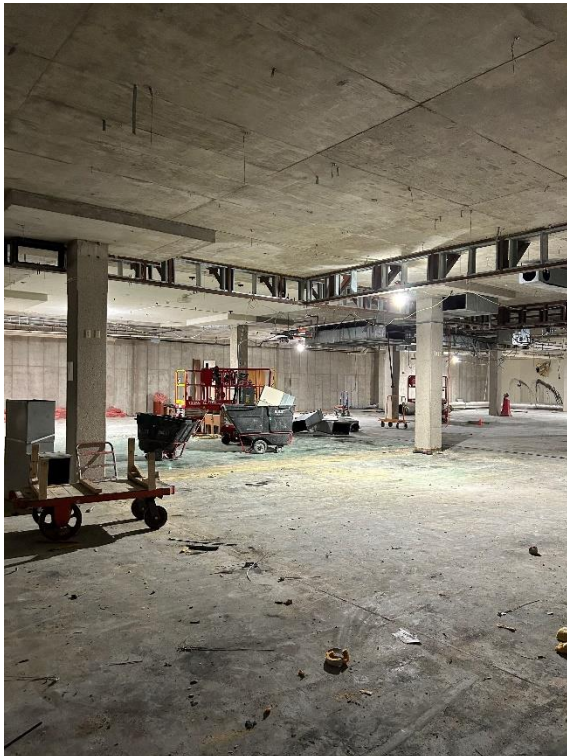

Northeast Lower Level

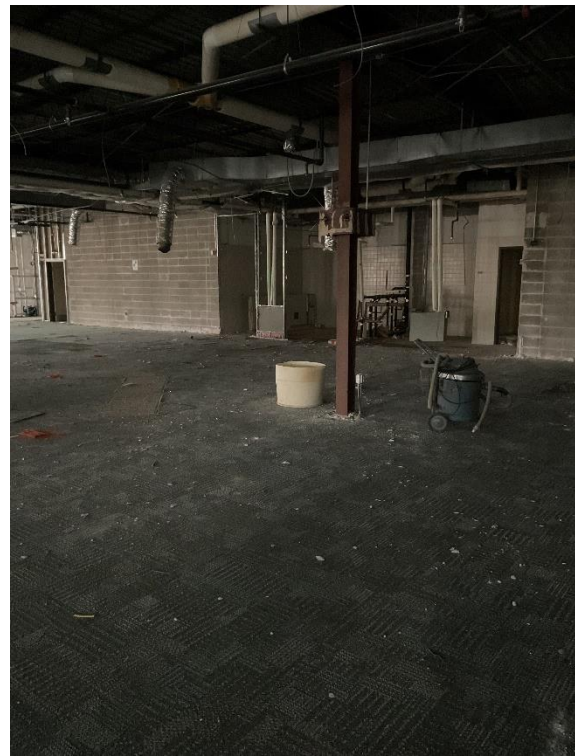

North Upper Level
