



© Skidmore, Owings & Merrill

BOLDT[®]
BUILD BOLDLY

February 2024

FEBRUARY REPORT

City of Appleton – Appleton Public Library

KEY PROGRESS POINTS

- Recycling Program:
 - Boldt continues to recycle items.
 - Weights to date of all metals are 365,305 lbs.

- Progress:
 - Received steel for Pavilion and miscellaneous metals.
 - Installed angles and decking at existing air shafts for concrete pour.
 - Completed angle bracing on Upper Level.
 - Demolition completed at freight elevator slab.
 - Started hanger installation on Upper Level.
 - Demolition building structure continues around existing elevator.
 - Continuing core drilling at locations verified and approved.
 - Began steel framing and concrete decking for floor at Pavilion.
 - Continuing saw cutting at freight elevator shaft.
 - CMU continues in shipping and receiving rooms on Ground Level, Mechanical Room on Upper Level, and passenger elevator shaft.
 - Continued MEPFP rough-ins on Lower and Ground Levels.
 - Drywall top-out began on Upper Level.


CONDITIONS & SAFETY

- Site conditions still remain very good. Continuously monitoring our safety program and making sure workers and the public are safe.
- Snow and ice plan have been implemented. Snow removal and salting is occurring as needed. Outside work continues to include 15 minutes or less during bitter cold weather days.
- There have been no injuries to date.

PROGRESS PHOTOS



Ground Level Flooring Steel

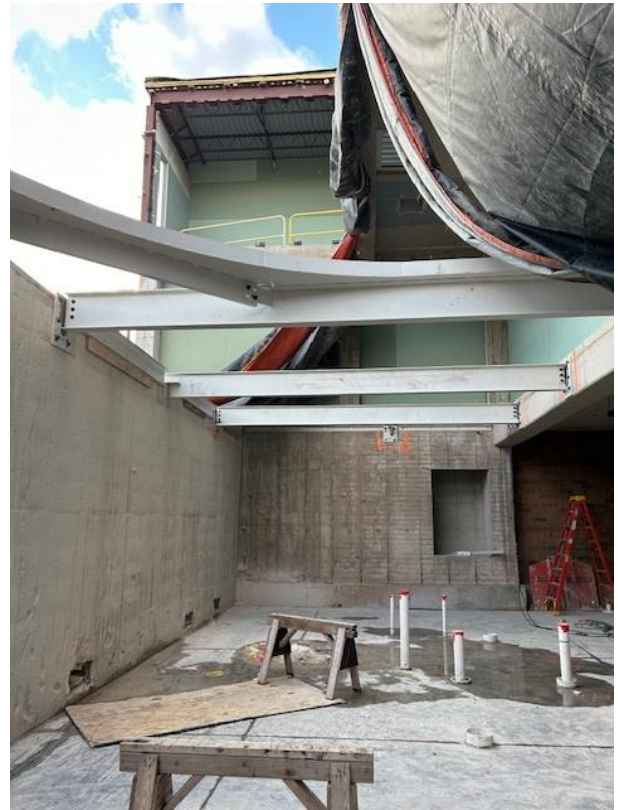

Ground Level Flooring Steel



Freight Elevator – Upper Level



Freight Elevator – Upper Level

PROGRESS PHOTOS




Footing at Pavilion Foundation Wall



Foundation Wall at Pavilion



Foundation Wall at Pavilion

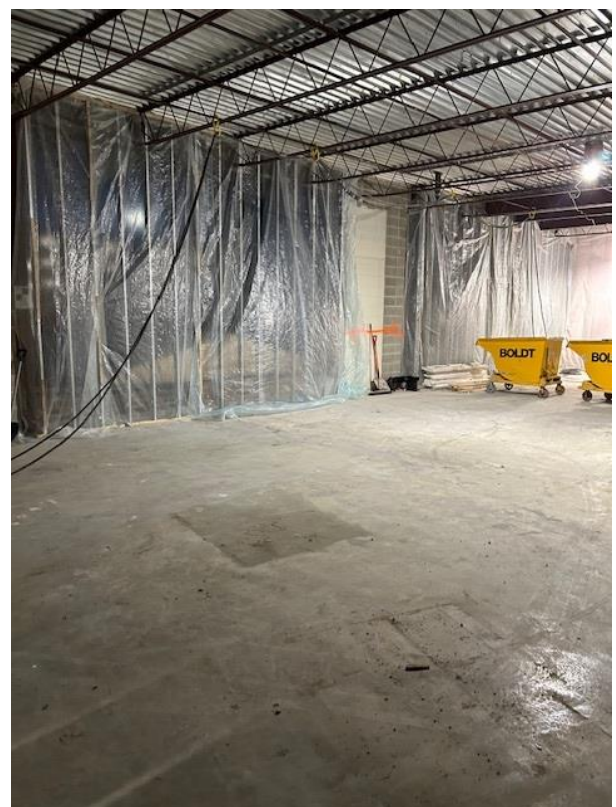

East Wall Demo for Overbuild
