



© Skidmore, Owings & Merrill

BOLDT[®]
BUILD BOLDLY

November 2023

NOVEMBER REPORT

City of Appleton – Appleton Public Library

KEY PROGRESS POINTS

- Recycling Program:
 - Boldt continues to recycle items, as necessary.
 - Weights to date of all metals are 334,845lbs.

- Progress:
 - Completed removal and storage of catwalk from East Side roof.
 - Air shaft demolition on the East end of the atrium on the Lower Level is completed.
 - Removed atrium mechanical room.
 - We completed the roofing demo meeting with the roofing contractor, SOM, and Boldt team.
 - Demolition continues on the Ground Level: North side atrium wall, brick façade, and CMU at atrium.
 - Concrete cutting for electrical and plumbing completed at Lower Level.
 - Underground electrical and plumbing has begun.
 - Removal of mechanical fans and motors in the Upper Level began.
 - Continuing layout for all floor penetrations for scanning of rebar and review.
 - Demolition continues for the freight elevator concrete slab and saw cutting for the Upper-Level passenger elevator opening.
 - Continuing demolition on the North Side and East Side Upper-Level façade.
 - Select roofing demolishing at East skylight is taking place.
 - Continuing aluminum framing and glazing removal on North atrium wall.


CONDITIONS & SAFETY

- Site conditions still remain very good. Continuously monitoring our safety program and making sure workers and the general public are safe.
- There were no injuries this month.

PROGRESS PHOTOS




Mechanical Room

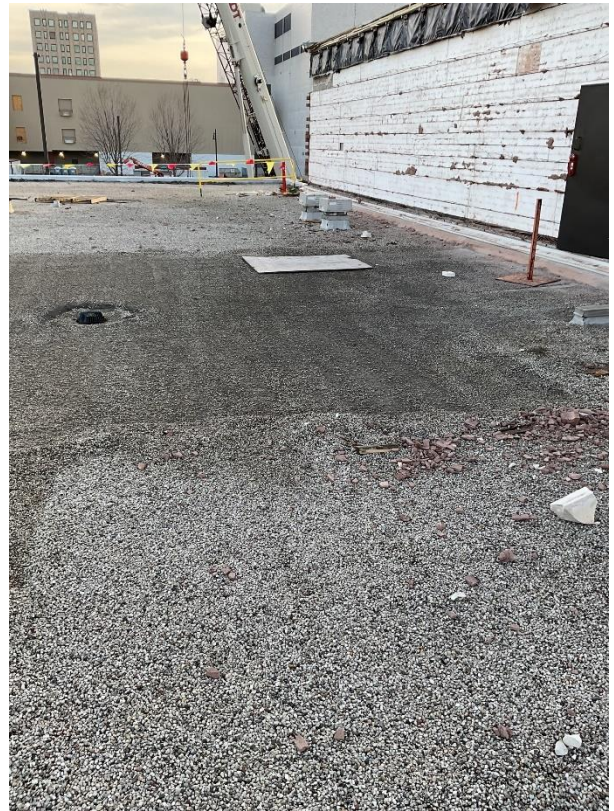

Lower Roof



Lower Level – North Side

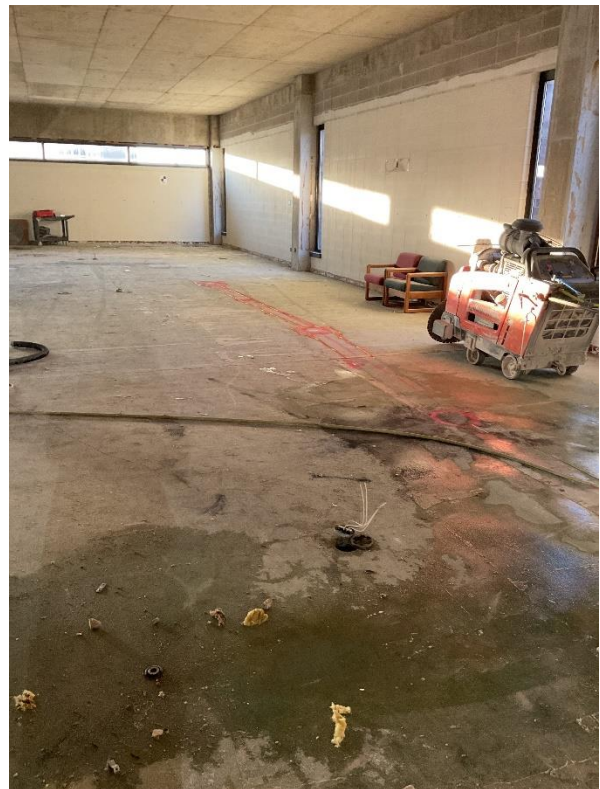


Ground Level – North/West Side

PROGRESS PHOTOS



Atrium

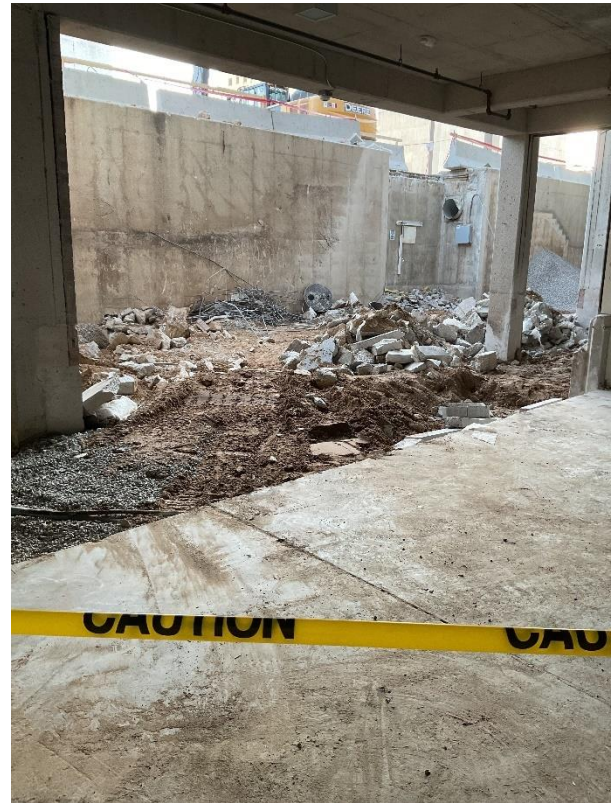

Atrium
