



December 2023

DECEMBER REPORT

City of Appleton – Appleton Public Library



KEY PROGRESS POINTS


- The Appleton Public Library project team won 2nd place in the Boldt Decorating Contest, with the Wisconsin Christmas Theme, in the job trailer!
- Recycling Program:
 - Boldt continues to recycle items, as necessary.
 - Weights to date of all metals are 354,845lbs.
- Progress:
 - Concrete was poured at Lower Level at electrical and plumbing trenches.
 - o Continued with demolition at freight elevator, West façade, and Northeast façade.
 - Started scanning floors for rebar locations at all thru-floor penetrations.
 - Continuing select roof demolition for steel install at over-build.
 - o Concrete slab cutting at Lower Level for freight elevator was completed.
 - Underpinning continues to be ongoing at passenger and freight elevator locations.
 - Iron workers will be starting to install steel for the freight elevator and West skylight.
 - Began exterior window in-fills.
 - o Installed steel and pour-in concrete at demoed ductwork at floor openings.
 - o Began reinforcing steel beams at Upper Level.
 - Layout for walls on Ground and Upper floors completed. Began the insulation install of upper and lower track, and MEP layout openings in-walls for framing.
 - Began installing door frames on Ground Level.
 - Completed excavating and forming of footings for addition.
 - Starting to form piers and foundation walls for addition.

CONDITIONS & SAFETY


- Site conditions still remain very good. Continuously monitoring our safety program and making sure workers and the general public are safe.
- There were no injuries this month.



PROGRESS PHOTOS

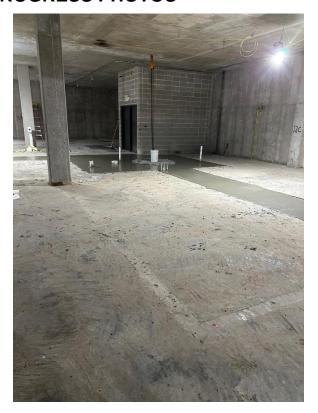


Lower Level – Plumbing Trench

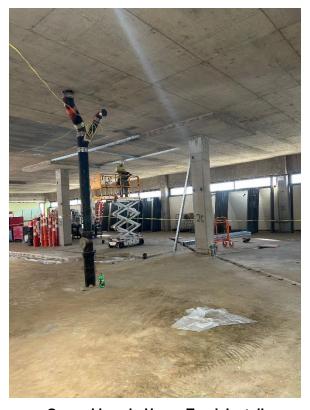

Ground Level - Upper Track Install




Lower Level – Plumbing Trench

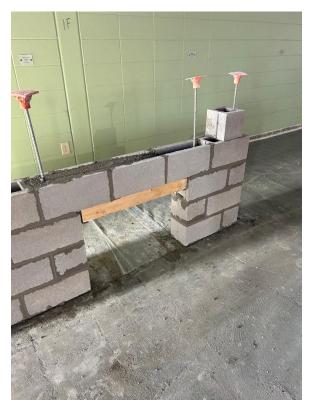


CMU Mock-Up




PROGRESS PHOTOS

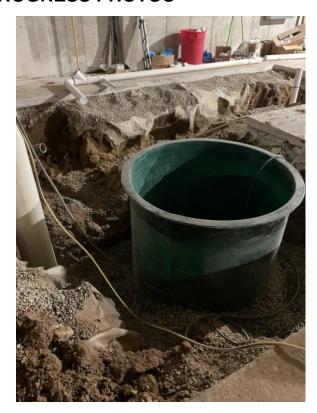

Lower Level - Sump Pit

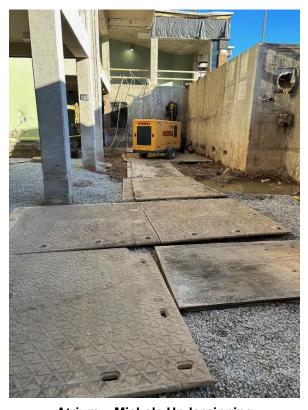

Atrium – Michels Underpinning

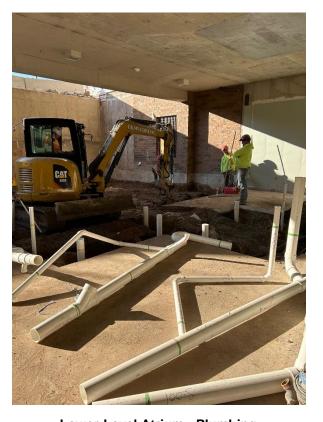

Lower-Level Atrium - Plumbing



Trailer Christmas Decorations
